



SEEF AVENUE II

THE HEIGHT OF COUTURE LIVING

PROGRESS REPORT - DECEMBER 2022

EXPERIENCE
THE HEIGHT OF
COUTURE
LIVING



www.seefavenue.com

 **Kooheji**
الكوهجي

SEEF AVENUE II PROJECT IS PROGRESSING AT A STEADY PACE

- Superstructure work for the typical floor slab & roof – Completed till 16th floor
- Block work – Completed till 11th floor
- Plastering work – Completed till 8th floor
- MEP services conducting & sleeve (1st Fix)
– Work in progress on 5th & 6th floor
- Mockup apartment – Work in progress

PROJECT PROGRESS

TYPICAL FLOOR

- Structural work 11/23 = 50%
- Block work 6/23 = 25%.
- Plastering work 4/23 = 15%
- MEP 1st fix 3/23 = 10%

PARKING FLOOR LEVEL

- Blockwork - 4/4 = 100%
- Plaster - 4/4 = 100%
- MEP 1st Fix work - 2/4 = 50%

CONSTRUCTION PROGRESS

CASTING WORK

Completed till 15th floor

BLOCK WORK

Completed till 10th floor

PROJECT MILESTONES



ELEMENT	ACTIVITY	PROGRESS
Sub Structure works	Pile head	100%
	Raft slab	100%
	Tie beam	100%
Super structure works - Car parks P1 to P4 levels	Column	100%
	Slab	100%
	Block works	100%
	Plastering	100%
Super structure works - Typical floor 5th - 10th floor levels	Mep	50%
	Column	100%
	Slab	100%
	Block works	100%
	Plastering	40%
Super structure works - Typical floor 11th - 15th floor levels	Mep	15%
	Column	100%
	Slab	100%
	Block works	20%

PROJECT MILESTONES



Project completion date
30 June 2024

Project Handover date
31 December 2024

Structure completion
April 2023

PICTORIAL REPRESENTATION OF STRUCTURE WORKS


KEY LEGEND

Baseline Dates (RCC)	
Work completed (RCC)	
Block work completion	

Piling
March 22 & April 22 (2 months)

Sub structure
May 22 & June 22 (2 months)

Super structure
1st July 22 to 31st July 23 (13 months)

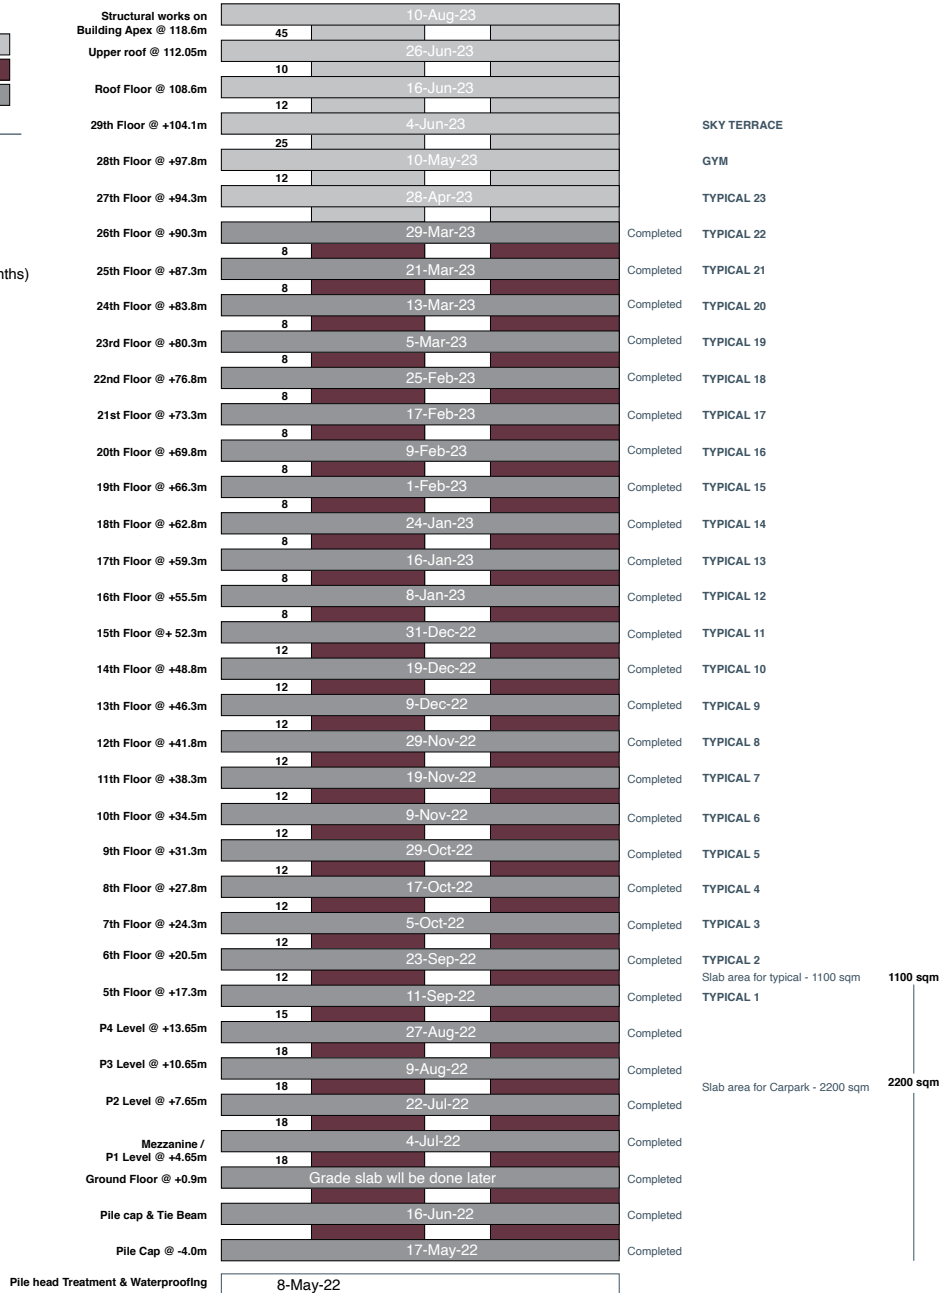

Aug 2022

Substructure 100%

Superstructure 15%

Dec 2022

Substructure - 100%


Superstructure - 50%

Blockwork - 25%

Plastering - 15%

External Plastering - 20%

MEP works - 15%.

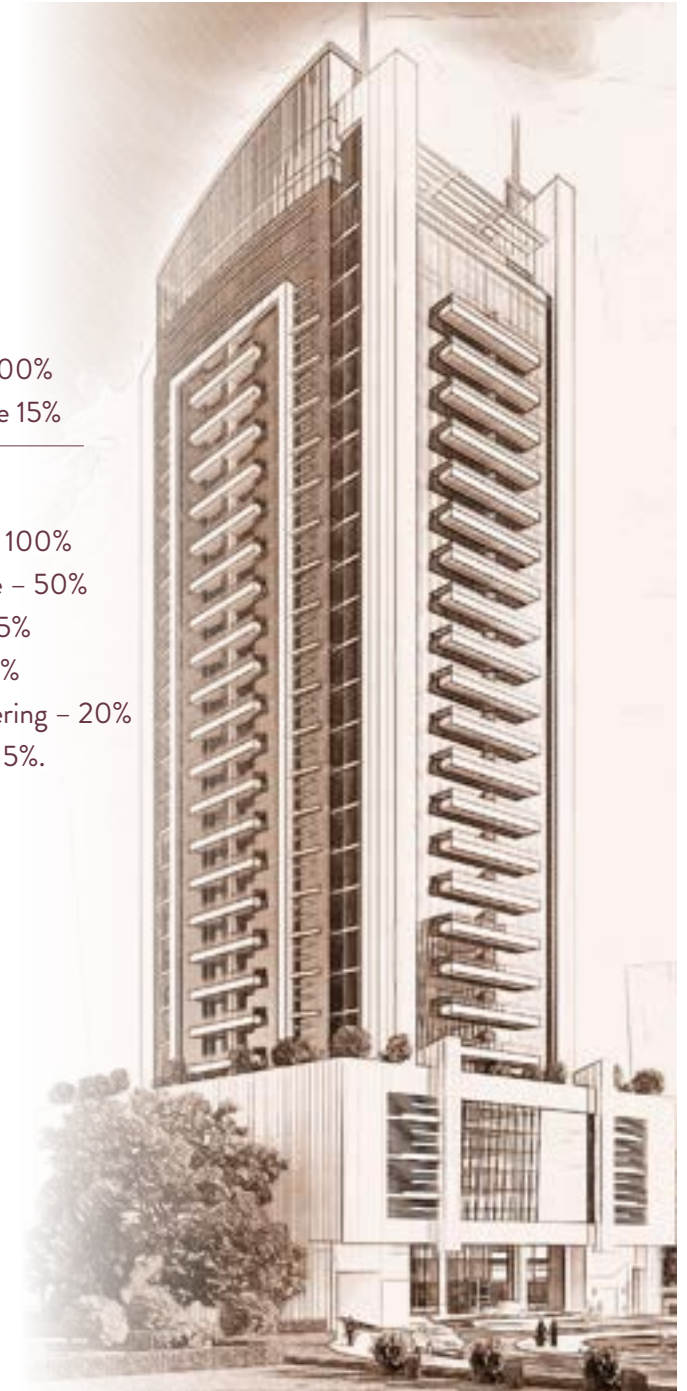

CONSTRUCTION WORKS



Block work in progress

Slab concreting work in progress



CONSTRUCTION WORKS

The Project Construction Manager during the site visit inspecting the progress of the mockup apartments

AC duct installation work is under progress



CONSTRUCTION WORKS

Wall finishes measurement checking
by our engineers



Rebar/MEP conducting works for the slab
is under progress



MEET THE TEAM



Chief Executive Officer
KOOHEJI DEVELOPMENT
Engr. Mohamed Abdulghaffar Al Kooheji

SALES TEAM



Property Advisor
Khalil Mohammed
Mobile: +973 32169858
khalil@rabahrain.com



Senior Property Advisor
Yahya Hassan Al Madani
Mobile: +973 66720802
yahya@rabahrain.com



SEEF AVENUE II

THE HEIGHT OF COUTURE LIVING



CLICK HERE TO VIEW
PROGRESS VIDEO

DEVELOPED BY

